


Thank you Big Sky for your patience and kindness to those who are working on this vital community project.

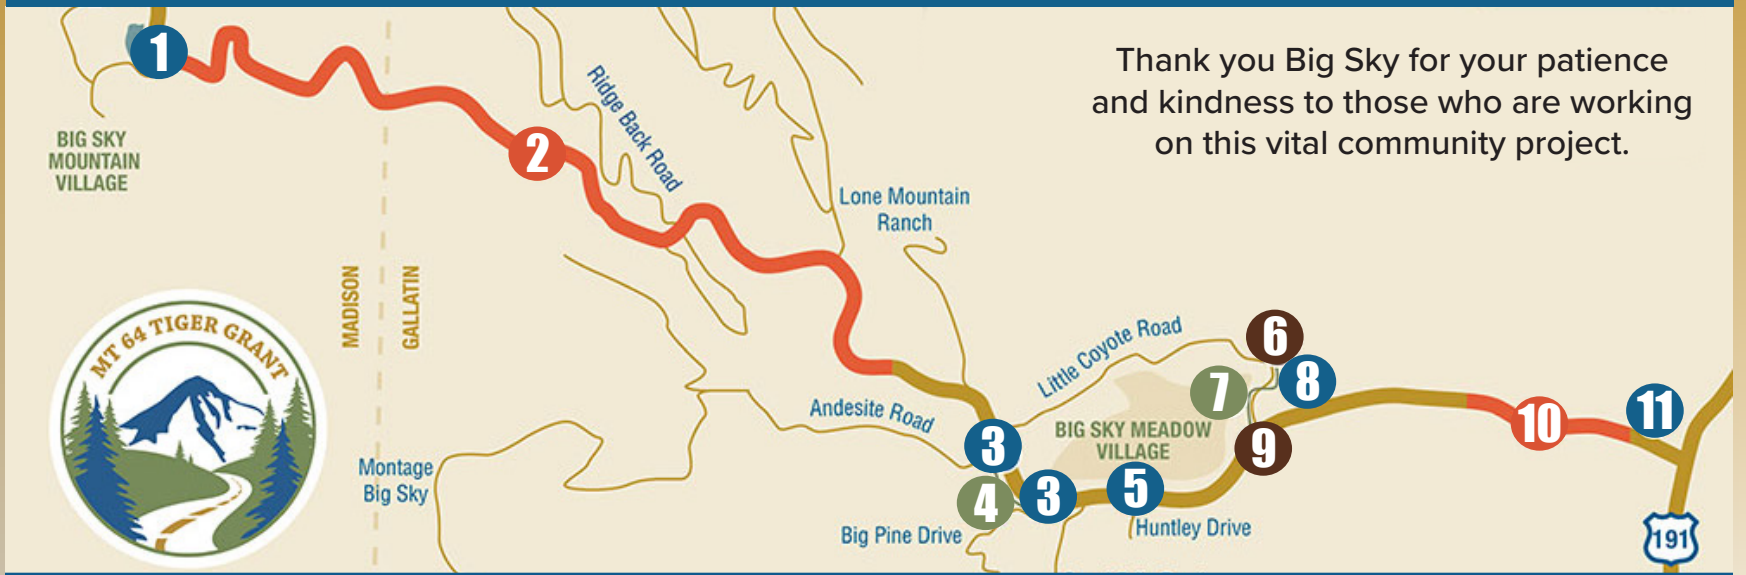

## 6 LITTLE COYOTE PEDESTRIAN BRIDGE

*Status:* Bridge is installed and path construction remains

*Percent complete:* 95%

*Remaining work:* Railing adjustments and final cleanup

*Anticipated completion:* Bridge should be complete in August, but won't be open for use until shared-use path paving is completed in September

## 7 LITTLE COYOTE SHARED-USE PATH

*Status:* Construction underway

*Percent complete:* 85%

*Remaining work:* Concrete and asphalt paving

*Anticipated completion:* Paving end of September



## 9 LITTLE COYOTE PEDESTRIAN TUNNEL

*Status:* Pedestrian tunnel in place, and backfilling and paving underway

*Percent complete:* 75%

*Remaining work:* Finish grading, guardrail, railing, seeding, etc

*Anticipated completion:* August



## 8 LITTLE COYOTE SIGNAL & TURN LANES

*Status:* Signal bases, electrical and stand up poles installed, and widening for turn lanes is underway

*Percent complete:* 30%

*Remaining work:* Concrete, signal, paving, pavement markings, and ADA ramps

*Anticipated completion:* Paving end of September, temporary pavement markings and signal turn-on anticipated for October, and chip seal and final markings in 2024

## 3 ANDESITE TO BIG PINE SHARED-USE PATH

*Status:* Construction of retaining walls underway

*Percent complete:* 30%

*Remaining work:* Path construction after walls are completed

*Anticipated completion:* Walls completed late August, path paving end of September, and railing, signage, seeding in October

## 4 LEFT-TURN LANES AT ANDESITE & BIG PINE DRIVE

*Status:* Not started | *Percent complete:* 0%

*Anticipated time frame:* Paving anticipated for end of September

## 2 SIGNAGE UPGRADES (CURVE WARNING, WILDLIFE, ETC.)

*Status:* Not started | *Percent complete:* 0%

*Anticipated time frame:* Complete fall of 2023

## 1 LEFT-TURN LANE AT BIG SKY RESORT ROAD

*Status:* Not started | *Percent complete:* 0%

*Anticipated time frame:* Work will take place in 2024

## 11 US 191 AREA

*Status:* Not started | *Percent complete:* 0%

*Anticipated time frame:* Work will take place in 2024

## 5 TURN LANE AT HUNTLEY

*Status:* Widening underway, single lane closures, and flaggers

*Percent complete:* 20%

*Remaining work:* Finish building road base for widening and paving

*Anticipated completion:* Paving end of September

Thank you to all the partners who are improving this corridor for everyone who travels to and around Big Sky: Federal Highway Administration, Montana Department of Transportation, Big Sky Resort Area District, Gallatin County and Madison County Commissions, Sanderson Stewart, and Riverside Contracting.

Dates are estimates.

Visit [mdt.mt.gov/pubinvolve/mt64](https://mdt.mt.gov/pubinvolve/mt64) for more project information.

